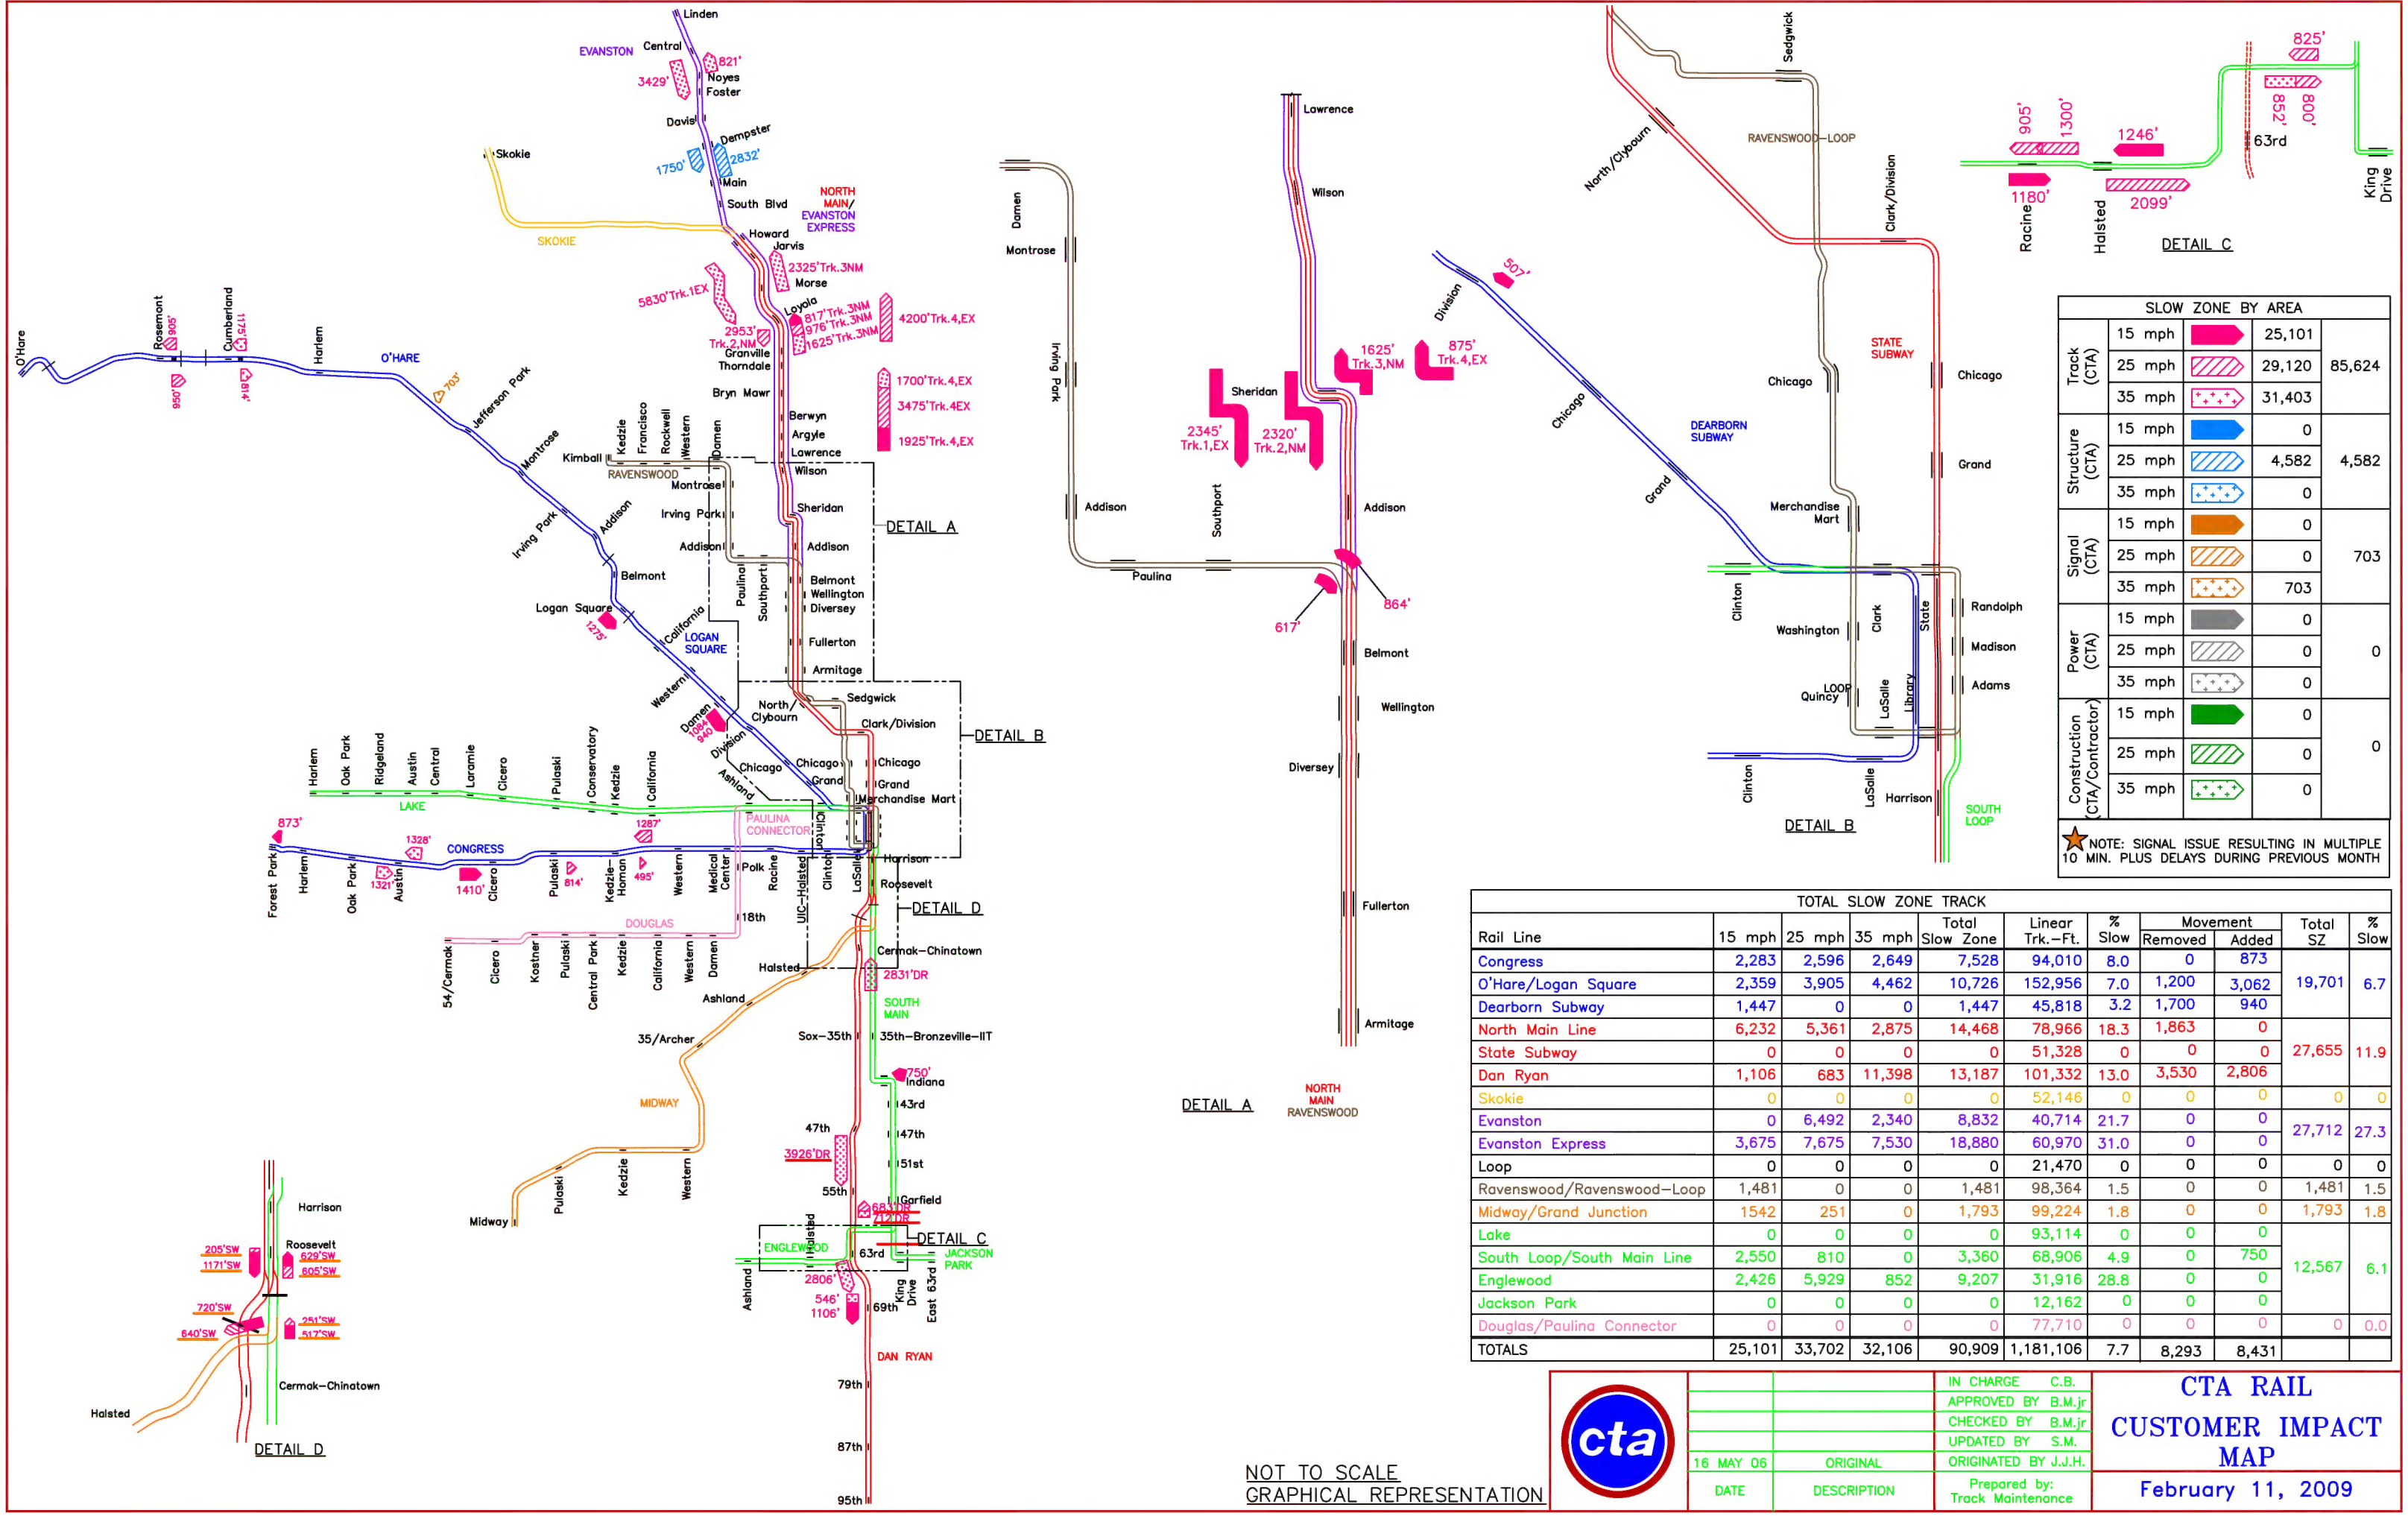

NOT TO SCALE
GRAPHICAL REPRESENTATION

SLOW ZONE BY AREA				
Track (CTA)	15 mph		25,101	85,624
	25 mph		29,120	
	35 mph		31,403	
Structure (CTA)	15 mph		0	4,582
	25 mph		4,582	
	35 mph		0	
Signal (CTA)	15 mph		0	703
	25 mph		0	
	35 mph		703	
Power (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Construction (CTA/Contractor)	15 mph		0	0
	25 mph		0	
	35 mph		0	

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK										
Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	2,283	2,596	2,649	7,528	94,010	8.0	0	873	19,701	6.7
O'Hare/Logan Square	2,359	3,905	4,462	10,726	152,956	7.0	1,200	3,062		
Dearborn Subway	1,447	0	0	1,447	45,818	3.2	1,700	940		
North Main Line	6,232	5,361	2,875	14,468	78,966	18.3	1,863	0	27,655	11.9
State Subway	0	0	0	0	51,328	0	0	0		
Dan Ryan	1,106	683	11,398	13,187	101,332	13.0	3,530	2,806		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	6,492	2,340	8,832	40,714	21.7	0	0	27,712	27.3
Evanston Express	3,675	7,675	7,530	18,880	60,970	31.0	0	0		
Loop	0	0	0	0	21,470	0	0	0	0	0
Ravenswood/Ravenswood–Loop	1,481	0	0	1,481	98,364	1.5	0	0	1,481	1.5
Midway/Grand Junction	1542	251	0	1,793	99,224	1.8	0	0	1,793	1.8
Lake	0	0	0	0	93,114	0	0	0	12,567	6.1
South Loop/South Main Line	2,550	810	0	3,360	68,906	4.9	0	750		
Englewood	2,426	5,929	852	9,207	31,916	28.8	0	0		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0.0
TOTALS	25,101	33,702	32,106	90,909	1,181,106	7.7	8,293	8,431		

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL CUSTOMER IMPACT MAP

February 11, 2009
